



Granite Hill Road Reconstruction Phase II 08/01/2025

Construction Activities & Upcoming Work

Project Number:

OR FLAP Grant 24(2)

FHWA Contact:

Alex Machupa

alex.machupa@dot.gov

(360)619-7745

Project Partner:

Wallowa Whitman National
Forest

Contractor:

Cascade Civil Corp

255 SE Black Butte Blvd

Redmond, OR

97756

Notice to Proceed:

February 28, 2025

Fixed Completion Date:

October 21, 2025



U.S. Department
of Transportation

**Federal Highway
Administration**

Project Description:

The Granite Hill Road Reconstruction Phase II project is a continuation of work that is being completed in the Wallowa Whitman National Forest near the town of Granite, OR. This project will replace five existing fish passage culverts. Three of the culverts will be replaced with precast concrete box culverts. The other two culverts will be replaced precast concrete bridges. Work also related to this project will contain streambed mitigation and restoration to the impacted areas.

Road Conditions:

Extreme caution should be used by motorist and tourist, particularly during rainy or snowy weather conditions. Temporary traffic control signs are utilized at the active construction locations to ensure public safety.

Current and Upcoming Work:

The contractor has continued the rip rap placement at Both bridge sites. At Bull Run #3 the UHPC pour is scheduled for Monday of next week. Work at Bull Run #1 and Boundary Creek box culverts will continue into next week. The contractor plans to se the final 2 wing walls for the Boundary Creek Box Culvert. At Bull Run #1 the contractor has started placing the form work and plans to pour the cut off wall.

Traffic Delays:

Minimal delays should be expected next week and the majority of the construction season. Please use caution when driving by construction operations.

Construction Mile Stones:


Bridge Locations:

- Temporary Bridge Installation
- Pile Driving
- Abutment Concrete Pour
- UHPC Linguodental Joints

Culvert Locations:

- Removal Of Existing Culvert
- Installation Of Box Culvert
- Streambed Material
- Streambed Restoration

Western Federal Lands Highway Division

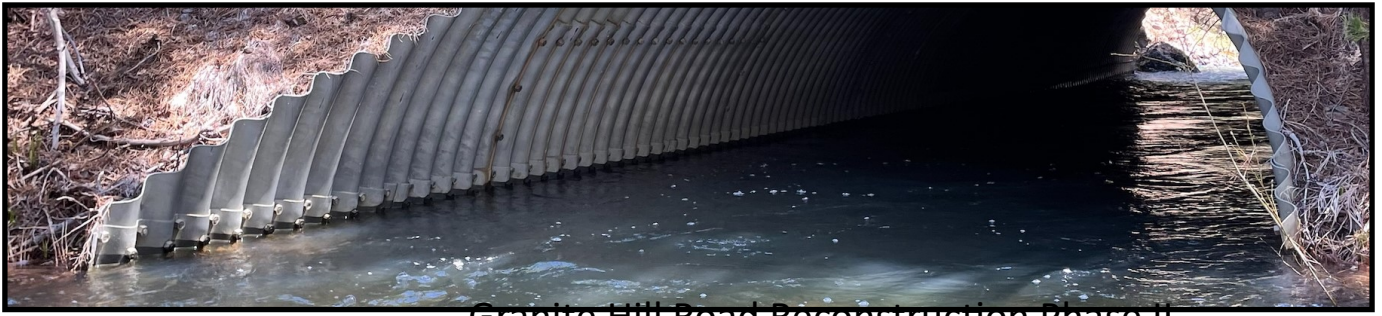

Granite Hill Road Reconstruction Phase II

08/01/2025

Construction Activities & Upcoming Work

Project Number:

OR FLAP Grant 24(2)

FHWA Contact:

Alex Machupa

alex.machupa@dot.gov

(360)619-7745

Project Partner:

Wallowa Whitman National
Forest

Contractor:

Cascade Civil Corp

255 SE Black Butte Blvd

Redmond, OR

97756

Notice to Proceed:

February 28, 2025

Fixed Completion Date:

October 21, 2025



U.S. Department
of Transportation

**Federal Highway
Administration**



Bull Run #1 Cutoff Wall Forms



Rip Rap Bull Run #4

Source: FHWA

Western Federal Lands Highway Division
