

POLYCHROME AREA IMPROVEMENTS



Source: proHNS

September 17, 2025

Construction Activities and Upcoming Work

Project Number:

AK NPS DENA 10(49)

FHWA Contact:

David Harvey

E: Jesse.Harvey@dot.gov

P: 360-833-3338

Project Partner:

National Park Service (NPS)

Contractor:

Granite Construction Co.
Anchorage, AK

Notice to Proceed:

1/4/2023

Fixed

Completion Date:

July 6, 2026

After a few weeks of wind delays, and the contractor waiting on material deliveries, work resumed and it's been a flurry of activity. The bridge is across and welded to the bearings on each side. The receiving tower at abutment 2 and the rest of the launch truss has been removed and staged for demobing. The back, cheek and wing walls have been set and are being welded at the east abutment. Preparations are being made to begin the final stages of thermosiphon installation and activation, along with backfill and grading at the east abutment. The slide has seen some extreme movement lately and has resulted in access down and across the slide being closed.


Traffic Delays

There are no traffic delays expected.



Source: proHNS

Rail Welding Backwall

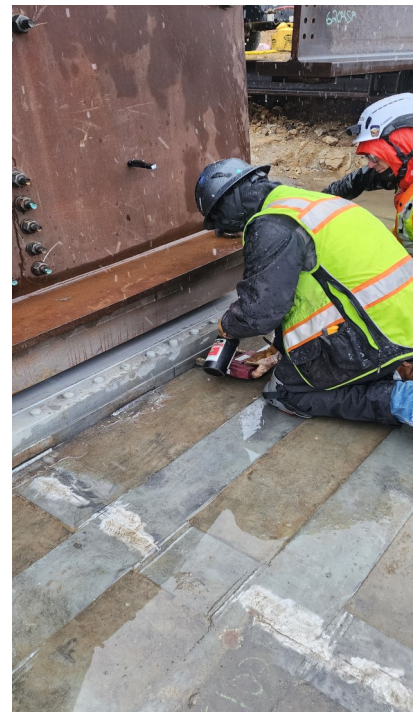

Source: proHNS

Mag Particle Testing Bering Welds



U.S. Department
of Transportation

**Federal Highway
Administration**

Website: <https://highways.dot.gov/federal-lands/projects/ak/nps-dena-10-49>

Western Federal Lands Highway Division
