

# OKANOGAN-WENATCHEE 2017 REPAIRS, PHASE 3

## CONSTRUCTION NEWSLETTER

October 2, 2020

### Project Number:

WA FS ERFO  
2017(1)-23(3)

### FHWA Contact:

Terry Hager  
terry.hager@dot.gov  
(360) 773-6341  
610 East Fifth Street  
Vancouver, WA 98661

### Project Partner:

USFS - Okanogan-  
Wenatchee National  
Forest

### Contractor:

Cates & Erb, Inc.  
Omak, WA

### Notice to Proceed:

March 23, 2020

### Completion Date:

Fall 2020

Project Website: <https://highways.dot.gov/federal-lands/projects/wa/fs-erfo-2017-1-23-3>



U.S. Department  
of Transportation

Federal Highway  
Administration

## Construction Activities

Work at Forest Service Road (FSR) 4010-050 MP 0.78 and MP 2.3 will continue next week. The 96-inch pipe culvert at MP 2.3 has been installed and backfilled. Work on the roadway grade over the pipe culvert is also moving forward. The concrete for the concrete collars for the inlet and outlet is expected to be poured next week.

The excavation work for the 132-inch pipe culvert at FSR 4010-050 MP 0.78 is expected to be completed next week along with the placement of the pipe culvert. FSR 4010-050 is closed to the public traffic during the work at MP 0.78 and MP 2.3.

Work at FSR 4200-400 MP 0.2 is underway, with the work focusing on a new riprap lined ditch near the current location of the USFS road closure gate. Work at the site will also include relocating the USFS road closure gate to a new location closer to the junction with FSR 4200.

The work on FSR 4200 is also underway. The work on FSR 4200 includes ditch repair and roadway reconditioning. Public traffic traveling on FSR 4200 near the junction with FSR 4200-400 will encounter delays during this work. Public traffic will be allowed thru the work area on FSR 4200 as work activities allow or during non-working periods. FSR 4200-400 is closed to public traffic during the work at MP 0.2.



Please, if the closed signs are up, stay out of the work area.

Also, use caution on roads nearby these sites, as there will be increased traffic related to work activities.


## Road Impacts

- **Closed** - FSR 4200/4200-400 MP 0.2
  - Work underway
  - FSR 4200-400 - Closed at junction with FSR 4200
  - FSR 4200 - Expect delays
- **Closed** - FSR 4010-050 MP 0.78 & MP 2.3
  - Work underway



Above: FSR 4200-400 MP 0.2

*Riprap staged for the upcoming riprap ditch work.*

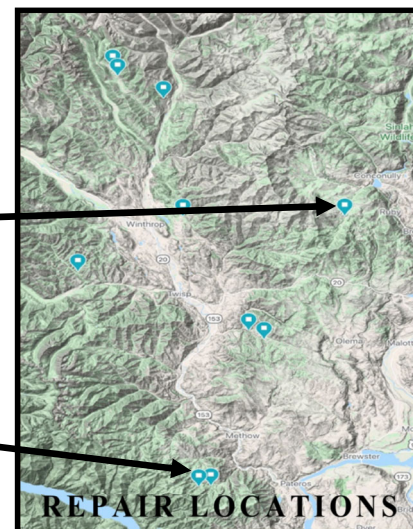

Western Federal Lands Highway Division
