

OKANOGAN-WENATCHEE 2017 REPAIRS, PHASE 3

CONSTRUCTION NEWSLETTER

October 9, 2020

Project Number:

WA FS ERFO
2017(1)-23(3)

FHWA Contact:

Terry Hager
terry.hager@dot.gov
(360) 773-6341
610 East Fifth Street
Vancouver, WA 98661

Project Partner:

USFS - Okanogan-
Wenatchee National
Forest

Contractor:

Cates & Erb, Inc.
Omak, WA

Notice to Proceed:

March 23, 2020

Completion Date:

Fall 2020

Project Website: <https://highways.dot.gov/federal-lands/projects/wa/fs-erfo-2017-1-23-3>



U.S. Department
of Transportation

Federal Highway
Administration

Construction Activities

Work at Forest Service Road (FSR) 4010-050 MP 0.78 and MP 2.3 will continue next week. At MP 2.3 the 96-inch pipe culvert is installed and backfilled. The contractor has begun work on finishing the roadway grade at the site. At MP 0.78 the excavation work for the 132-inch pipe culvert is expected to be completed early next week. Backfilling work is anticipated to be started by the end of next week with the roadway work at MP 0.78 taking place the following week. FSR 4010-050 is closed to public traffic during the work at MP 0.78 and MP 2.3.

Work at FSR 4200-400 MP 0.2 will continue next week with the contractor finishing the grading and aggregate placement. The work on the new riprap lined ditch is complete and the USFS road closure gate has been relocated. On FSR 4200 the ditch repair and roadway reconditioning is complete with roadway grading underway. Work at FSR 4200/4200-400 MP 0.2 is expected to be completed early next week.

Public traffic on FSR 4200 near the junction with FSR 4200-400 will encounter delays during this work. Public traffic will be allowed thru the work area on FSR 4200 as work activities allow or during non-work periods. FSR 4200-400 is closed to public traffic during the work at MP 0.2.



Please, if the closed signs are up, stay out of the work area.

Also, use caution on roads nearby these sites, as there will be increased traffic related to work activities.


Road Impacts

- **Closed** - FSR 4200/4200-400 MP 0.2
 - Work underway
 - FSR 4200-400 - Closed at junction with FSR 4200
 - FSR 4200 - Expect delays
- **Closed** - FSR 4010-050 MP 0.78 & MP 2.3
 - Work underway



Above: FSR 4200-400 MP 0.2

New riprap lined ditch

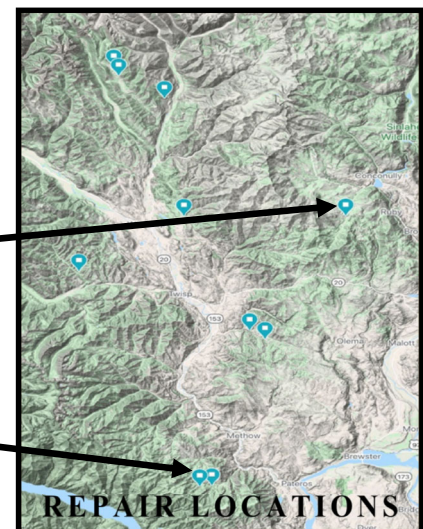

Western Federal Lands Highway Division
