



Yellowstone River Bridge August 16, 2024

Construction Activities & Upcoming Work

Project Description:

Utilizing Great American Outdoor Act Funding the Yellowstone River Bridge project includes constructing a new bridge over the Yellowstone River, a new alignment to the bridge approach, expansion of picnic areas, and additional parking at various trailheads.

Road Conditions:

Extreme caution should be used by motorist and tourist, particularly during rainy or snowy weather conditions. Temporary traffic control signs are utilized at the active construction locations to ensure public safety.

Current and Upcoming Work:

The contractor began coring for the bearing plates for Pier 3 cap and will continue into next week. Post tension strands for Pier 3 are scheduled to begin on Tuesday of next week. At Pier 2 the contractor stacked 2 segments with more segments arriving next week. Work continued with forming the Pier 2 Cap and installing the rebar. With the Pier cap planned to be poured on August 29th. The contractor started forming the Pier 1 cap with rebar installation to begin early next week. More girders were delivered this week. At the pre-cast plant segment 215 was casted last week. Segments for Pier 1 will start next week and will continue until completion with only 3 left to cast.

Traffic Delays:

Minimal delays should be expected next week and the majority of the construction season. Please use caution when driving by construction access roads.

2024 Construction Milestones:

Completion of Footings—Finished

Erection of pre-cast Pier Segments

- ◆ Pier 3—Complete
- ◆ Pier 2—In Progress
- ◆ Pier 1—Later this Season

Completion of Pier Caps

- ◆ Pier 3—Complete
- ◆ Pier 2—In Progress
- ◆ Pier 1—In Progress

Girder Erection—Later this Season

Project Website: <https://highways.dot.gov/federal-lands/projects/wy/nps-yell-12-2>

Project Number:

WY NPS YELL 12(2)

FHWA Contact:

Nathan Douglass

nathan.douglass@dot.gov

(208) 351-0054

Project Partner:

Yellowstone National Park

Contractor:

HK Contractors Inc.

P.O. Box 51450

Idaho Falls, Idaho

83402

Notice to Proceed:

January 24, 2023

Fixed Completion Date:

November 30, 2026



U.S. Department
of Transportation

**Federal Highway
Administration**

Western Federal Lands Highway Division



Yellowstone River Bridge August 16, 2024

Construction Activities & Upcoming Work

Project Number:

WY NPS YELL 12(2)

FHWA Contact:

Nathan Douglass

nathan.douglass@dot.gov

(208) 351-0054

Project Partner:

Yellowstone National Park

Contractor:

HK Contractors Inc.

P.O. Box 51450

Idaho Falls, Idaho

83402

Notice to Proceed:

January 24, 2023

Fixed Completion Date:

November 30, 2026




U.S. Department of Transportation

Federal Highway Administration



Overview of the Project Site

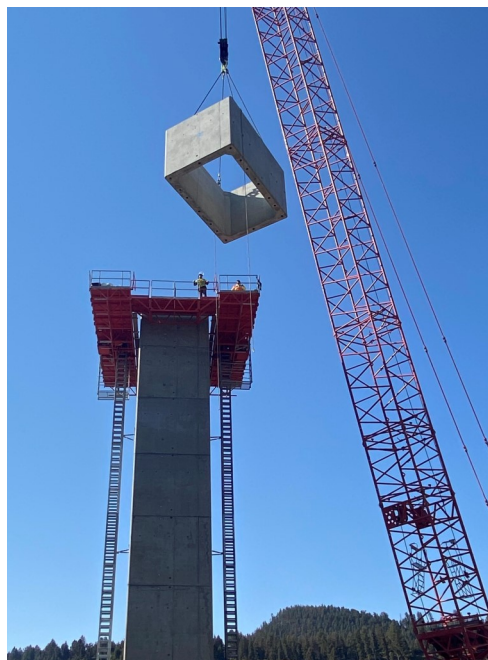

Stacking Pier 2



Pier 3 Girder Delivery

Source: FHWA

Project Website: <https://highways.dot.gov/federal-lands/projects/wy/nps-yell-12-2>

Western Federal Lands Highway Division
