


Yellowstone River Bridge



July 11, 2025

Yellowstone River Bridge

Construction Activities & Upcoming Work

Project Description:

Utilizing Great American Outdoor Act Funding the Yellowstone River Bridge project includes constructing a new bridge over the Yellowstone River, a new alignment to the bridge approach, expansion of picnic areas, and additional parking at various trailheads.

Road Conditions:

Extreme caution should be used by motorist and tourist, particularly during rainy or snowy weather conditions. Temporary traffic control signs are utilized at the active construction locations to ensure public safety.

Current and Upcoming Work:

Installation of the bridge underdrain system continues this week. At Abutment 2, embankment construction and Geosynthetic Reinforced Soil (GRS) backfill operations are complete. At Abutment 1, the concrete forms have been removed from Wingwall A and B. Backfill and grading has begun at Pier 1.

Out first, concrete deck pour was successfully completed on the night of July 8th. The next deck pour will take place on the night Friday, July 11th. Work continues on deck drain inlet installation and bridge deck rebar placement.

Traffic Delays:

Minimal traffic delays are expected through next week and for the remainder of the construction season. Drivers are reminded to exercise caution near construction access roads. Temporary traffic interruptions may occur as materials are delivered and crews access pier locations.

2025 Construction Milestones:

Completion of Abutments—In Progress
Girder Erection—Completed
Bridge Deck—In Progress
Road Realignment—Later This Season

Project Number:

WY NPS YELL 12(2)

FHWA Contact:

Nathan Douglass

nathan.douglass@dot.gov

(208) 351-0054

Project Partner:

Yellowstone National Park

Contractor:

HK Contractors Inc.

P.O. Box 51450

Idaho Falls, Idaho

83402

Notice to Proceed:

January 24, 2023

Fixed Completion Date:

November 30, 2026




U.S. Department
of Transportation

**Federal Highway
Administration**

Project Website: <https://highways.dot.gov/federal-lands/projects/wy/nps-yell-12-2>

Western Federal Lands Highway Division

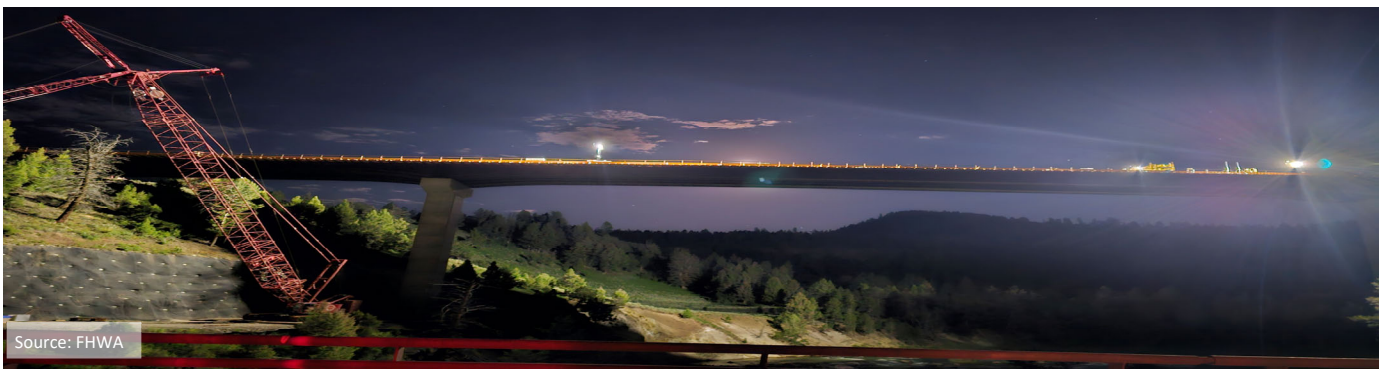

July 11, 2025

Yellowstone River Bridge Construction Activities & Upcoming Work

Project Number:

WY NPS YELL 12(2)

FHWA Contact:

Nathan Douglass

nathan.douglass@dot.gov

(208) 351-0054

Project Partner:

Yellowstone National Park

Contractor:

HK Contractors Inc.

P.O. Box 51450

Idaho Falls, Idaho

83402

Notice to Proceed:

January 24, 2023

Fixed Completion Date:

November 30, 2026




U.S. Department
of Transportation

**Federal Highway
Administration**



Waiting for Concrete.

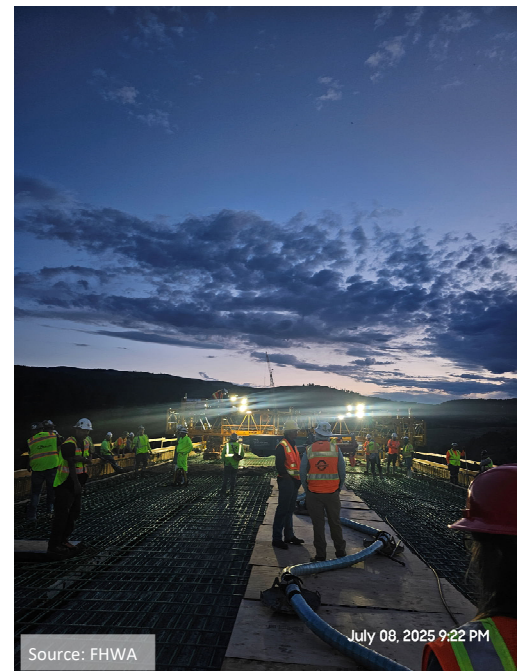


Start of First Deck Pour.

Project Website: <https://highways.dot.gov/federal-lands/projects/wy/nps-yell-12-2>

Western Federal Lands Highway Division

Yellowstone River Bridge

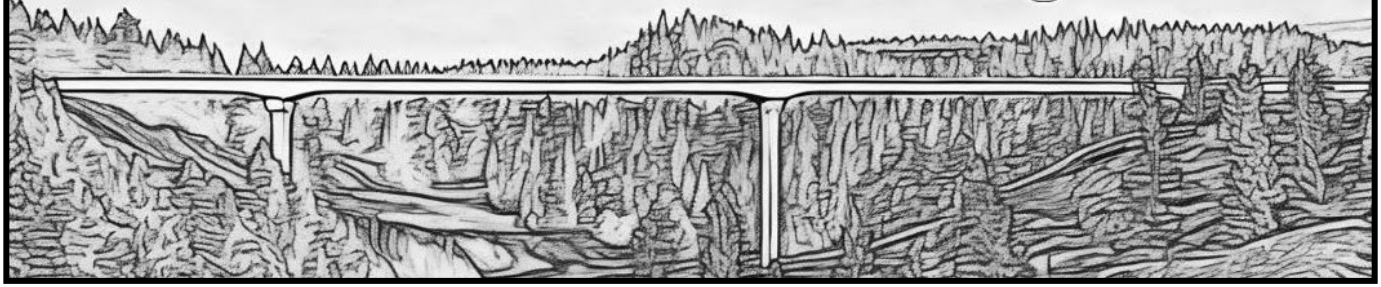

July 11, 2025

Yellowstone River Bridge

Construction Activities & Upcoming Work

Project Number:

WY NPS YELL 12(2)

FHWA Contact:

Nathan Douglass

nathan.douglass@dot.gov

(208) 351-0054

Project Partner:

Yellowstone National Park

Contractor:

HK Contractors Inc.

P.O. Box 51450

Idaho Falls, Idaho

83402

Notice to Proceed:

January 24, 2023

Fixed Completion Date:

November 30, 2026



U.S. Department
of Transportation

**Federal Highway
Administration**



Source: FHWA

Deck Pour at the
Finishing Phase.



Source: FHWA

Applying Tined Finish.



Source: FHWA

Application of Curing
Compound.

Project Website: <https://highways.dot.gov/federal-lands/projects/wy/nps-yell-12-2>

Western Federal Lands Highway Division
