

POLYCHROME AREA IMPROVEMENTS



Source: N. Weisman, NPS

July 27, 2023

Project Number:

AK NPS DENA 10(49)

FHWA Contact:

David Harvey
E: Jesse.Harvey@dot.gov
P: 360-833-3338

Project Partner:

National Park Service (NPS)

Contractor:

Granite Construction Co.
Anchorage, AK

Notice to Proceed:

1/4/2023

Current Fixed

Completion Date:

September 30, 2024

Anticipated Fixed

Completion Date:

July 1, 2026



U.S. Department
of Transportation

**Federal Highway
Administration**

Construction Activities and Upcoming Work


The contractor worked on developing their staging area at Bear Cave (approx. MP 44.8), and removed the stockpile of material that was staged at the Ghiglione Bridge pullout.

Survey work at the slide site will begin the end of this week and continue in support of the contractor during this phase of the work. Earthwork on the east side of the slide will begin Tuesday, August 1, with work to remove the “knob” on the south side of the road at the edge of the slide.

Traffic Delays

There are no traffic delays expected. The Denali Park Road is closed to the public beginning at mile post 43, the East Fork Toklat River Bridge.

In the next few days, you may notice some new temporary signage before and after the entrance to the MP 5 pit, warning of trucks entering the roadway.

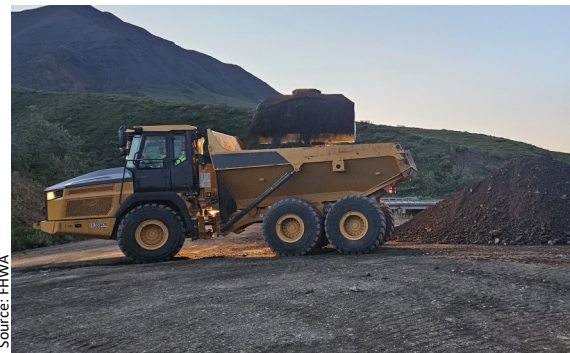

Source: FHWA

Removing stockpile from
Ghiglione Pullout

Installing temporary
culvert at the Bear Cave
staging area



Source: FHWA

Website: <https://highways.dot.gov/federal-lands/projects/ak/nps-dena-10-49>

Western Federal Lands Highway Division
