

# East Entrance Road—Fishing Bridge to Indian Pond



Project Number:

WY NPS YELL 13(11)

FHWA Contact:

Daniel Christianson

Daniel.Christianson@dot.gov

C: 406-217-7344

O: 307-242-7310

Lake Maintenance Station

BLDG 708

506 Howell Drive

PO Box 3308

Lake, WY 82190

Project Partner:

National Park Service -  
Yellowstone NP

Contractor:

Oftedal Construction, Inc.  
Miles City, MT

Notice to Proceed:

April 16, 2018

Fixed Completion Date:

October 30, 2020

## Construction Activities & Upcoming Work August 10, 2020



### Road Surface Conditions

The roadway is paved from the intersection at the Grand Loop Road to the west side of Pelican Creek and also from the east side of Pelican Creek to Indian Pond. The causeway across Pelican Creek remains gravel.



### Current and upcoming work

Current activities:

- The third deck pour for Frame 3 was completed on July 24.
- The concrete placement for Abutment 2 was done on August 5.
- Formwork/falsework continues for the middle spans (Frame 2).
- Stone Masonry work at the west abutment and wingwalls
- Continued placement and finishing of aggregate at the bridge approaches.
- Removal of the work bridge, beginning at the west end and working eastward.

Upcoming work:

- Continue installation of formwork and falsework for Frame 2.
- Nelson stud installation in Frame 2.
- Culvert cleaning at Fishing Bridge Visitor Center.
- Continue removal of the work bridge.
- Concrete placement for the approach slab at Abutment 1.
- Continue masonry work on the bridge and cobblestone medians.
- Asphalt paving at the Visitor Center, the east end of the project, and sidewalks.



Storm Water Pollution Prevention Plan (SWPPP): The SWPPP is available for viewing at Oftedal's project office.



Project Website: <https://flh.fhwa.dot.gov/projects/wy/east-entrance/>



U.S. Department  
of Transportation

**Federal Highway  
Administration**

**Western Federal Lands Highway Division**


# East Entrance Road—Fishing Bridge to Indian Pond

August 10, 2020

## Traffic Delays

Expect short delays Monday – Sunday. A combination of flaggers, traffic signals, and a pilot car may be used to control traffic.

The Gas Station, Repair Shop, and General Store are open in Fishing Bridge Village. The Visitor Center remains closed for the season.

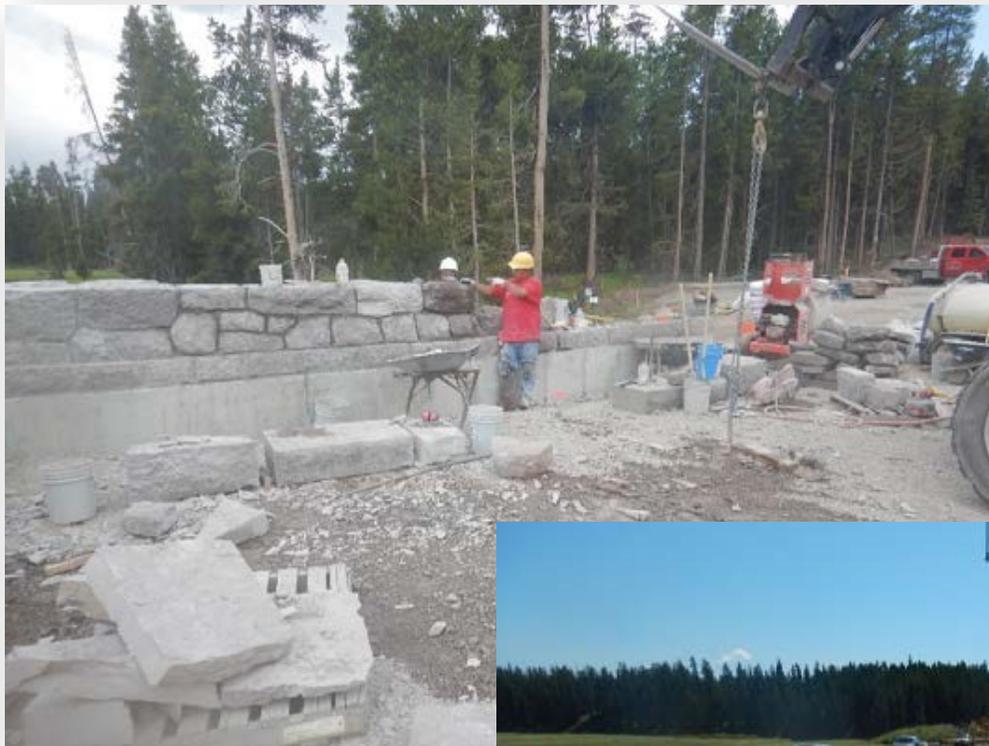

Masons setting stone facing for guardwall—west approach to Pelican Creek Bridge



Frame 2 deck formwork—Pelican Creek Bridge



U.S. Department of Transportation

**Federal Highway Administration**

**Western Federal Lands Highway Division**
