



Yellowstone River Bridge June 28, 2024

Construction Activities & Upcoming Work

Project Description:

Utilizing Great American Outdoor Act Funding the Yellowstone River Bridge project includes constructing a new bridge over the Yellowstone River, a new alignment to the bridge approach, expansion of picnic areas, and additional parking at various trailheads.

Road Conditions:

Extreme caution should be used by motorist and tourist, particularly during rainy or snowy weather conditions. Temporary traffic control signs are utilized at the active construction locations to ensure public safety.

Current and Upcoming Work:

The contractor has completed the backfill process for the footings at Pier 1 and 2. The MSE wall at Pier 2 was completed and at Pier 3 the contractor has been forming and tying rebar for the Pier Cap, with an anticipated pour date of July 11th. Pre-cast segments for Pier 2 arrived last week and the contractor will begin the erection process. Off-site at the pre-cast plant Pier 2 is nearing completion and then work will start will Pier 1 pre-cast segments once complete.

Traffic Delays:

Minimal delays should be expected next week and the majority of the construction season. Please use caution when driving by construction access roads. Weekend work will be ongoing this Saturday.

2024 Construction Milestones:

Completion of Footings—Finished
Completion of MSE wall at Pier 2—Finished
Erection of pre-cast Pier Segments

- ◆ Pier 3—Complete
- ◆ Pier 2—In Progress
- ◆ Pier 1—Later this Season

Completion of Pier Caps

- ◆ Pier 3—In Progress
- ◆ Pier 2—Later this Season
- ◆ Pier 1—Late this season

Girder Erection—Later this Season
Paving the Picnic Loops—Later this Season

Project Website: <https://highways.dot.gov/federal-lands/projects/wy/nps-yell-12-2>

Project Number:

WY NPS YELL 12(2)

FHWA Contact:

Nathan Douglass

nathan.douglass@dot.gov

(208) 351-0054

Project Partner:

Yellowstone National Park

Contractor:

HK Contractors Inc.

P.O. Box 51450

Idaho Falls, Idaho

83402

Notice to Proceed:

January 24, 2023

Fixed Completion Date:

November 30, 2026



U.S. Department
of Transportation

**Federal Highway
Administration**

Western Federal Lands Highway Division



Yellowstone River Bridge June 28, 2024

Construction Activities & Upcoming Work

Project Number:

WY NPS YELL 12(2)

FHWA Contact:

Nathan Douglass

nathan.douglass@dot.gov

(208) 351-0054

Project Partner:

Yellowstone National Park

Contractor:

HK Contractors Inc.

P.O. Box 51450

Idaho Falls, Idaho

83402

Notice to Proceed:

January 24, 2023

Fixed Completion Date:

November 30, 2026



U.S. Department
of Transportation


**Federal Highway
Administration**



Completed Pier 3 and Start of Pier 2



Completed Pier 3

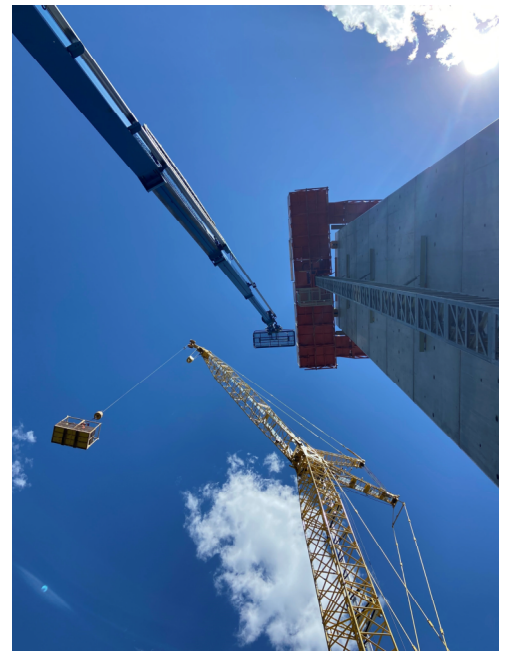

Inspection of Pier 3

Source: FHWA

Project Website: <https://highways.dot.gov/federal-lands/projects/wy/nps-yell-12-2>

Western Federal Lands Highway Division
