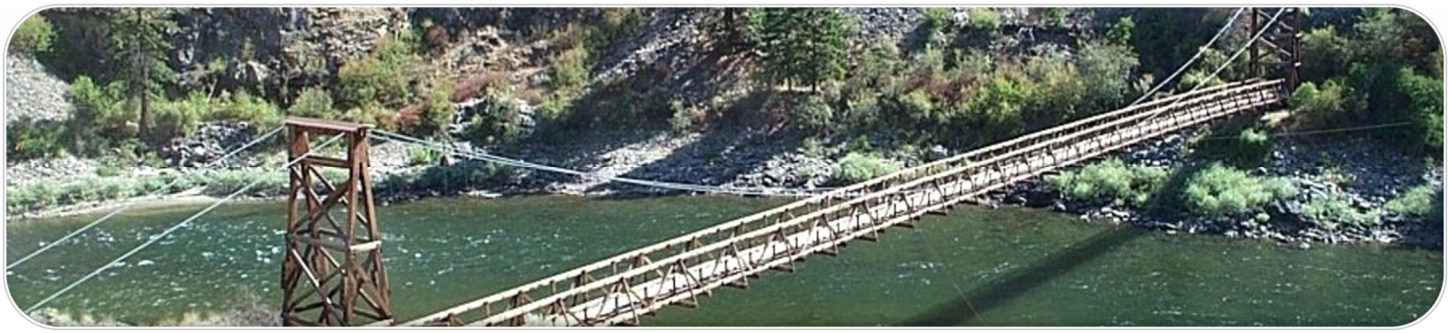

Stoddard Bridge

Salmon River Road (FS 30), 39 Miles West of North Fork, Idaho

October 10, 2025

Project Number:
ID FS ERFO 2017(1)-29(1)

FHWA Contact:
Todd Butikofer, PM
Todd.butikofer@dot.gov
(360)606-1445

Address:
SVBIC
803 Monroe St.
#110
Salmon, Idaho 83467

Contractor:
Inland Crane Inc.
6931 Supply Way
Boise, Idaho 83716-5540

Notice to Proceed:
June 17, 2022

Expected Completion Date:
Winter 2025/2026

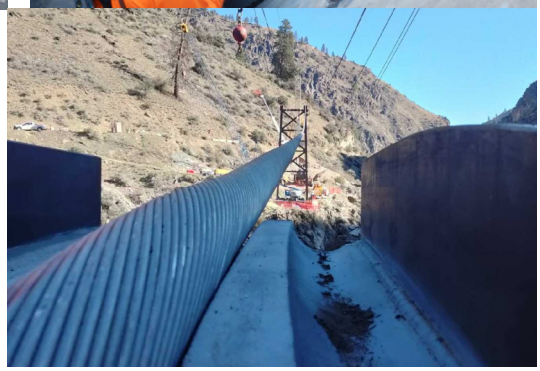

The first suspension cable B'

Source of photos: FHWA

Construction Activities & Upcoming Work

Inland Crane, Inc. (ICI) is continuing to work on the concrete finishing and backfill of Abutment 1 on the south side of the river. It has been quite a week with the first of 6 suspension cables being launched, flown, connected and set into the saddles with a lot of effort and persistence by ICI. The process will continue two more times on the up river side of the bridge before starting to install the hangers and hanger cables. Then moving and doing it all over again on the down river side of the bridge.

There will not be any work on-site over the Columbus Day holiday weekend.

With the tower and cable erection there could be short traffic delays of up to 20 minutes, to facilitate the erection of the bridge.

Please Use Caution when traveling and be aware of oncoming traffic, during day, night, weekdays, and weekends. It continues to be a single traffic lane through the construction site at the Crane Tower. Concrete barriers has been installed to protect the traveling public and the project site. The speed limit continues to be 15 mph thru this area during the 2025 Construction Season. Thank you for your cooperation and understanding.

Project Web Site: https://highways.dot.gov/federal-lands/projects/id/fs-erfo-2017-1-29-1

U.S. Department of Transportation
Federal Highway Administration

Western Federal Lands Highway Division
